

SalesForce Service Transition into Version One Managed Services

Executive Summary — Senior Service Transition Project Manager

CONFIDENTIAL · CLIENT DELIVERY

Project Overview

What We Are Delivering

This engagement represents a full-scale migration of the Salesforce Service Cloud environment into the Version One Managed Services platform — a strategic modernisation initiative designed to consolidate service operations, reduce overhead, and unlock scalable performance for the organisation's growing service demands.

Accountable leadership for all phases, decisions, and outcomes rests with the Senior Service Transition Project Manager, ensuring a single point of coordination across all workstreams.

Objective

Migrate Salesforce Service Cloud to the Version One Managed Services platform

Scope

Full transition of service operations, data migration, and process optimisation

Duration

18-month engagement with a structured, phased rollout approach

Strategic Business Outcomes

The transition to Version One Managed Services is anchored in three transformational value drivers that directly benefit the client's operational and strategic goals.



Cost Consolidation

Reduced operational costs through a unified managed services model, eliminating redundant tooling, licensing overhead, and fragmented support structures.



Enhanced Service Delivery

Measurably improved service delivery capabilities and customer satisfaction metrics, enabled by Version One's purpose-built managed services environment.




Scalability & Performance

Improved system scalability and sustained performance headroom to support the organisation's growing service demands without infrastructure constraints.

Project Timeline & Milestones

The engagement is structured across four sequential phases, each with defined deliverables and governance checkpoints to ensure controlled progression and risk containment.

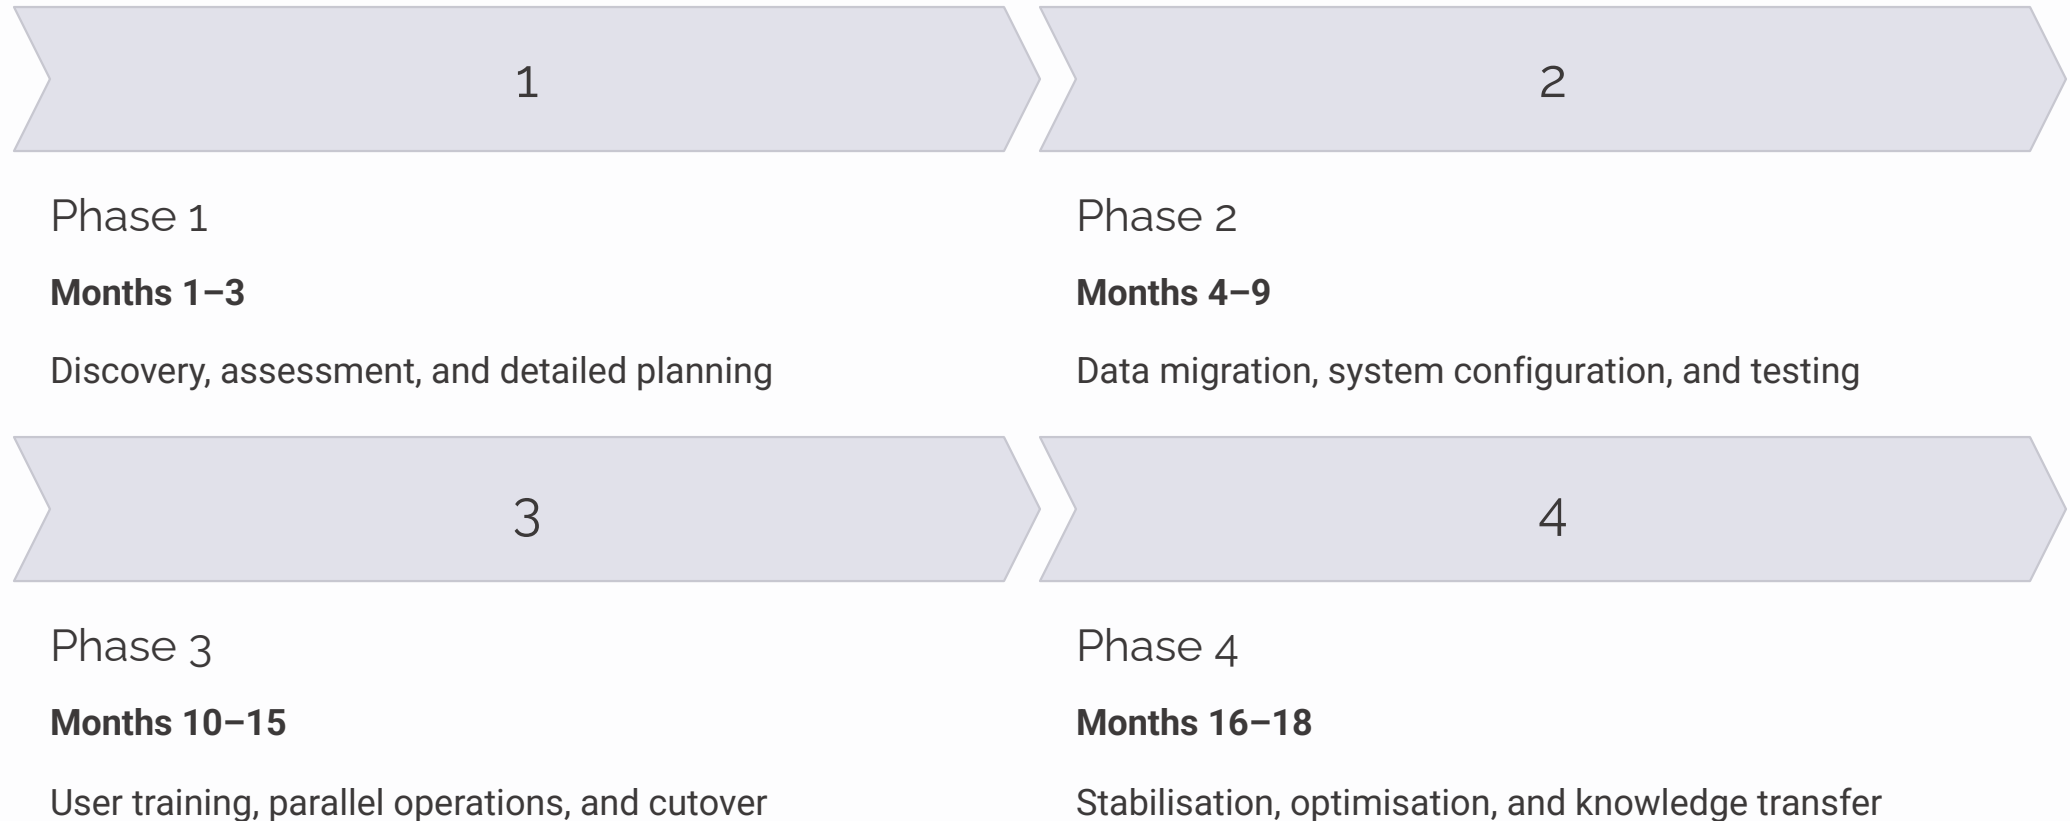

- ☐ Each phase concludes with a formal Steering Committee review and sign-off gate before progression to the next phase.

Team Structure & Governance

Accountability Model

The Senior Service Transition Project Manager holds overall accountability for delivery, acting as the primary interface between client leadership, the Version One implementation partner, and the core project team.

A formal Steering Committee provides executive oversight, strategic direction, and escalation resolution throughout the 18-month engagement.

Organisational Structure

Project Leadership

Senior Service Transition Project Manager — overall delivery accountability and client relationship management

Core Project Team

Technical architects, business analysts, QA specialists, and change management leads embedded across all workstreams

Steering Committee

Executive sponsors, client leadership, and Version One representatives providing governance and strategic oversight

Technical Implementation Approach

The technical strategy is engineered for precision, minimising disruption to live service operations while ensuring complete data fidelity and seamless system continuity throughout the transition.

API-Driven Data Migration

All data migration is executed via a structured API framework with embedded validation checkpoints at each stage. This approach ensures traceability, supports automated reconciliation, and enables rollback procedures if anomalies are detected during transfer.

Custom Workflow Configuration

Version One workflows are configured to mirror and optimise existing Salesforce service processes. Configuration is validated against documented business rules prior to any parallel operation or cutover activity.

Enterprise System Integration

Full integration is maintained with existing enterprise systems including ERP, CRM, and ticketing platforms, ensuring no interruption to cross-system data flows and reporting continuity during and after transition.

Resource Allocation & Budget

Resource Deployment

12 FTE

Internal project team members spanning technical, analytical, and change management disciplines

External Partners

Version One implementation partner supplemented by specialist consultants for targeted workstreams

Budget Framework


The project budget is structured across four primary investment categories, with contingency reserves allocated to protect against scope volatility and risk materialisation.

- **Technology:** Platform licensing, infrastructure, and tooling
- **Labour:** Internal FTE and external consultancy costs
- **Training:** Curriculum development, delivery, and support
- **Contingency:** Reserve allocation for risk and scope management

- Budget tracking and variance reporting are presented at each Steering Committee review cadence.

Risk Management Strategy

A proactive risk management framework is in place across the full project lifecycle. The following primary risk categories have been identified, assessed, and assigned dedicated mitigation and contingency responses.

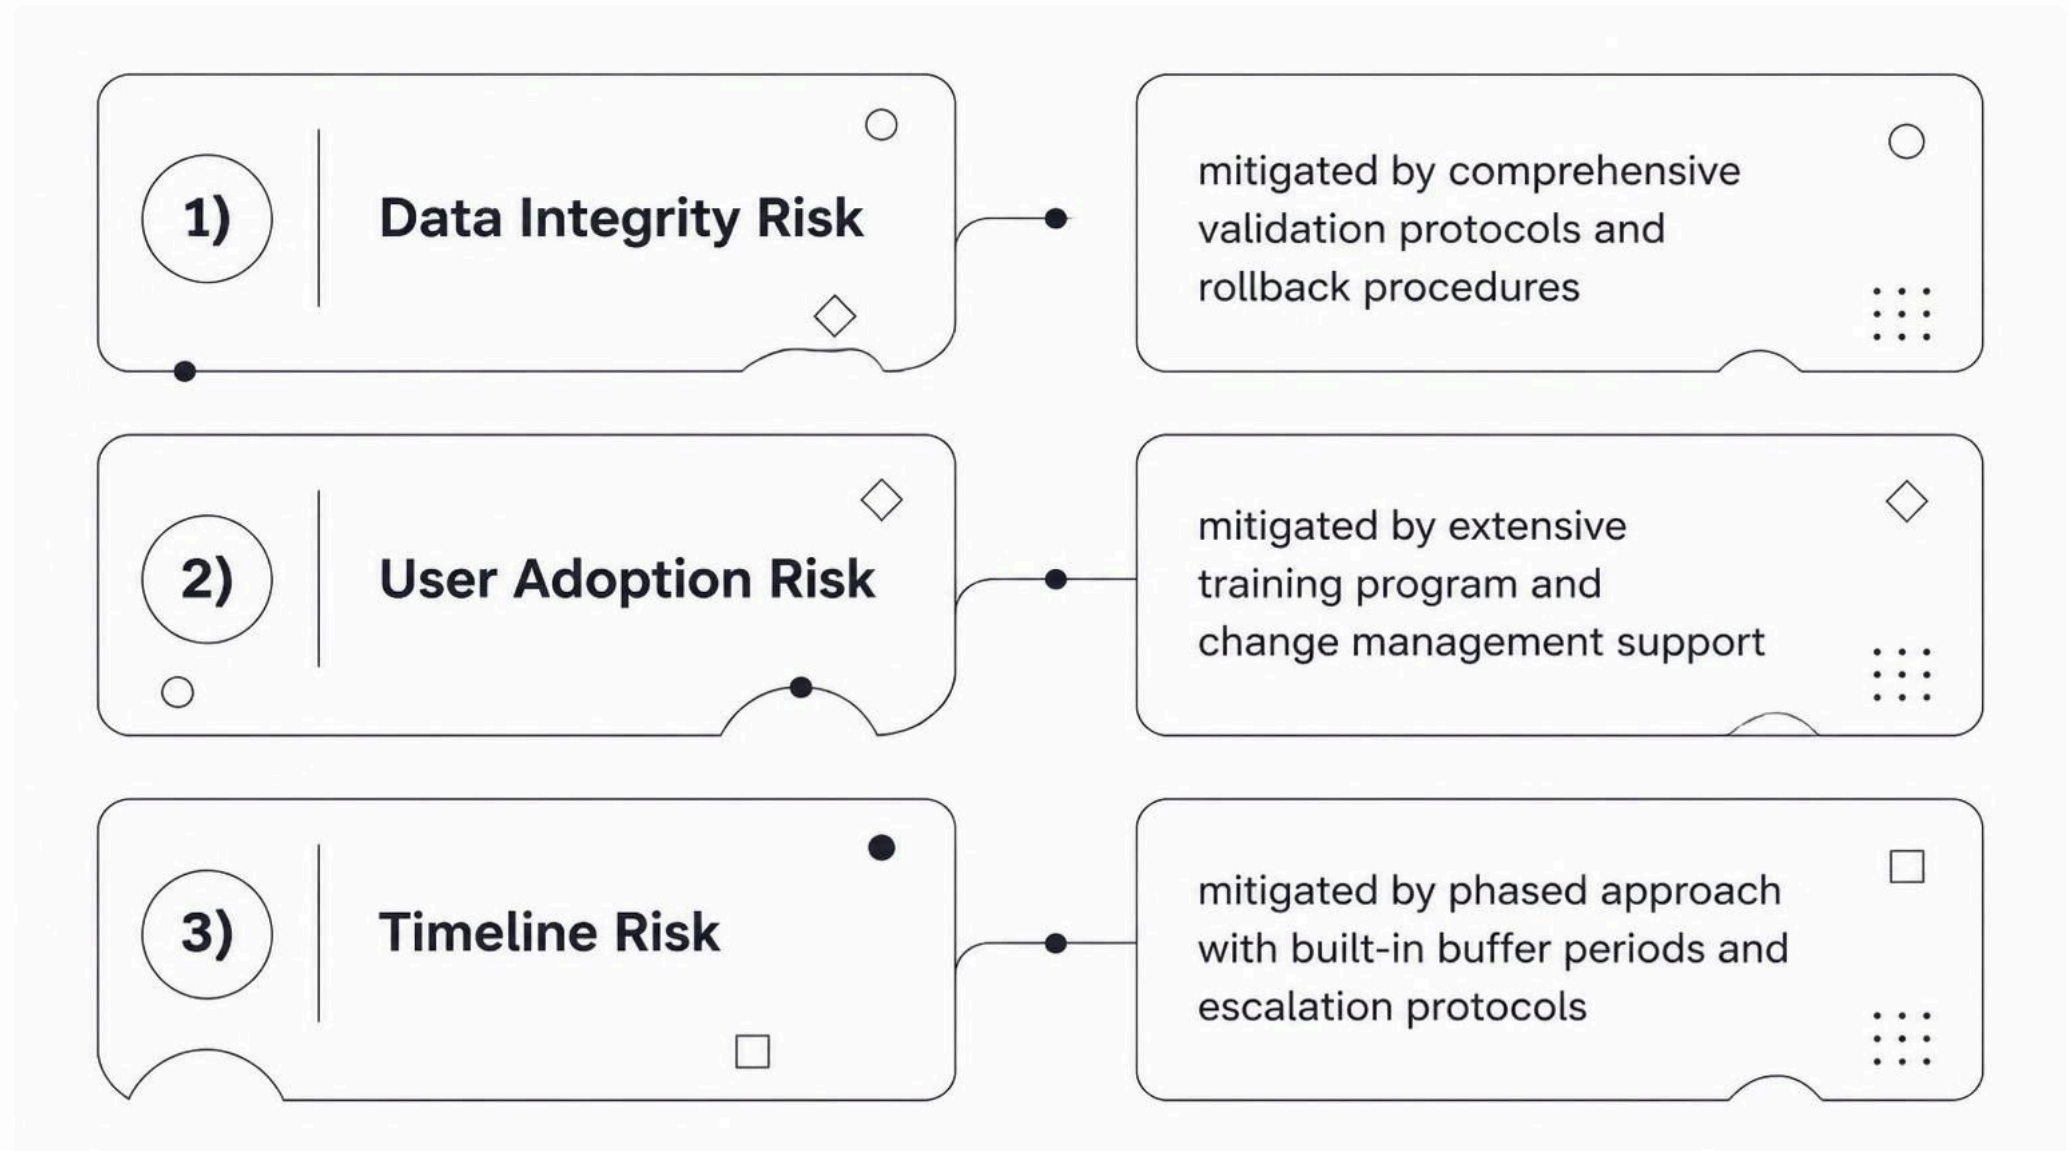

All risks are tracked on a live risk register, reviewed bi-weekly by the project leadership team, and escalated to the Steering Committee when risk scores exceed defined thresholds.

Change Management & Training

People-First Transition Philosophy

Sustainable adoption of the Version One platform requires structured, people-centred change management from day one. The change programme runs in parallel with technical delivery – not as an afterthought – to ensure readiness at every phase gate.

The Senior Service Transition Project Manager retains direct oversight of the change management workstream, ensuring alignment between technical milestones and organisational readiness.

01

Stakeholder Engagement

Structured engagement plan with regular communication cadence, tailored messaging by stakeholder group, and executive briefing schedule throughout the project lifecycle

02

Training Curriculum

Comprehensive role-based training programme covering all user groups, delivered through blended learning formats with competency validation prior to go-live

03

Post Go-Live Support

Dedicated hypercare support period following cutover, with structured continuous optimisation reviews and a knowledge transfer programme to embed capability in-house

Success Metrics & KPIs

Project success is measured against four non-negotiable performance indicators. These metrics are baselined at project initiation and reported against at each Steering Committee review and at project closure.

On-Time & On-Budget Delivery Full 18-month delivery within approved schedule and budget parameters, with variance tracking at each phase gate	Zero Critical Data Loss Complete data integrity maintained throughout migration, validated by reconciliation checkpoints and sign-off at each migration batch
>90% User Adoption Adoption rate exceeding 90% across all user groups within 60 days of go-live, measured by platform usage analytics and competency assessments	SLA Compliance Service level agreement compliance maintained at or above baseline throughout the full transition period – no degradation in service quality to end customers

❏ These KPIs form the basis of the project closure report and will be formally signed off by the Steering Committee upon project completion.
